


# FORTNIGHTLY UPDATE 05.05.23

## Saint Ignatius College Mackillop Senior Centre

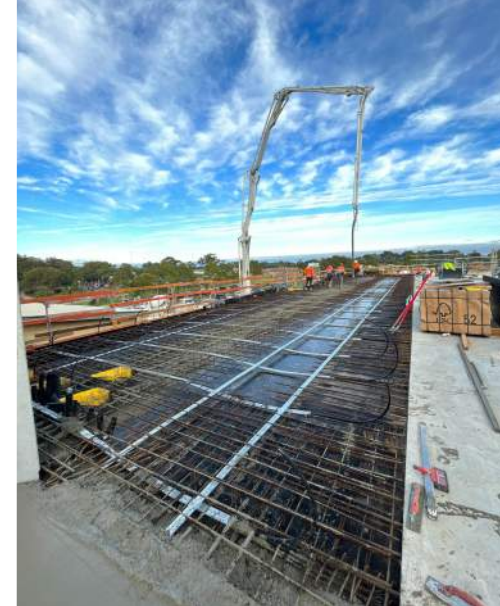

Over the past fortnight, we closed out some of the major work items. This included the key milestone of our last major concrete pours to level 2 and the project! This area includes the learning deck which overlooks the northern landscape. We also completed installation of all pre-cast panels today, amounting to 140 panels in total across all levels. This will be acknowledged through an official Top Out Ceremony.

All propping to the theatre is currently being removed, allowing services to commence. Stair formwork has now begun to the north which will link level 1&2. Shrouds have also started to be installed along the east elevation. With majority of rough-in service works wrapping up on north ground floor, electrical and mechanical services have now commenced on level 1 north. This is due to the roof sheeting and insulation being installed, allowing a fast track approach.

We also welcome our new member to the STIGS team, Brett Benson who will assist with site coordination throughout the duration of the project

### UPCOMING TASKS

- Complete wall framing & setout on north level 1
- Complete window shroud install
- Complete north ground services to memorial garden
- Steel installation to south level 2
- Complete prop removal to lecture theatre

### COMPLETED TASKS

- Concrete pour to south level 2
- Installation of roof to level 1 north
- All pre-cast installation
- Shrouds on east elevation
- Concrete footings for east link way
- Storm water pits to memorial garden
- Roof sheeting to north Level 1

### YOUR PROJECT TEAM



Alex Simpson  
Project manager



Paul Hunt  
Site manager



Adam McPhee  
Site Foreman



Jacob Bunn  
Contract Administrator



Caroline Andrus  
Contract Administrator

For further enquiries, please email our project team;  
STIGS@PLANGROUP.COM.AU
