

FORTNIGHTLY UPDATE 07.11.2022

SAINT IGNATIUS COLLEGE | MACKILLOP SENIOR CENTRE

Plan Group and our subcontractors have completed our first major milestone in pouring the south ground floor slab, along with preparation for the northern ground floor slab. The in-ground services are all but complete in the northern section.

We have a very busy fortnight ahead, with major structural elements taking place. We are eagerly anticipating the north concrete pour & commencement of precast panels to the southern areas. Look-out for the big 250tonne crane onsite when we are lifting precast panels into place!

Despite the terrible weather that October has brought us, we are still making significant progress onsite .

One more final push for the VCE students to get to the finish line... Goodluck everyone!




COMPLETED TASKS

- Completion of ground level south pours
- Manufacture of precast panels for Ground Level
- Inground services for North slab
- Steel & precast shop drawings all but complete (Refer to model image on the right)

UPCOMING TASKS

- Strip formwork for ground level south pours
- Preparation for north slab pour, formwork & reinforcement
- Commence precast panel installation
- Post-tensioning, mechanical, windows & glazing shop drawings well underway

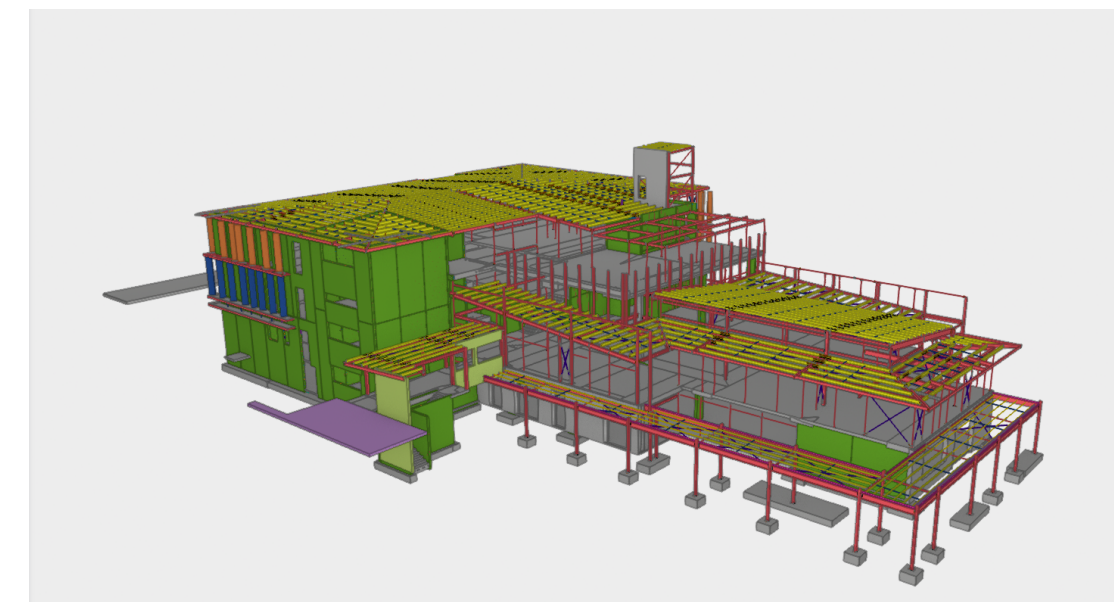

YOUR PROJECT TEAM



Alex Simpson
Project Manager



Paul Hunt
Site Manager



Adam McPhee
Site Foreman



Jacob Bunn
Contract Administrator

For further enquiries, please email our project team below;
STIGS@PLANGROUP.COM.AU

