


FORTNIGHTLY UPDATE 30.06.23


Saint Ignatius College Mackillop Senior Centre



North East

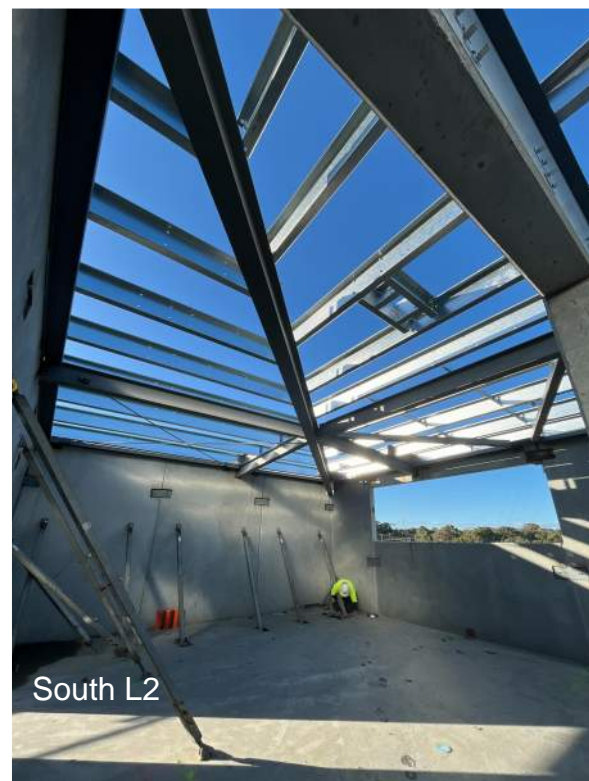

South L2

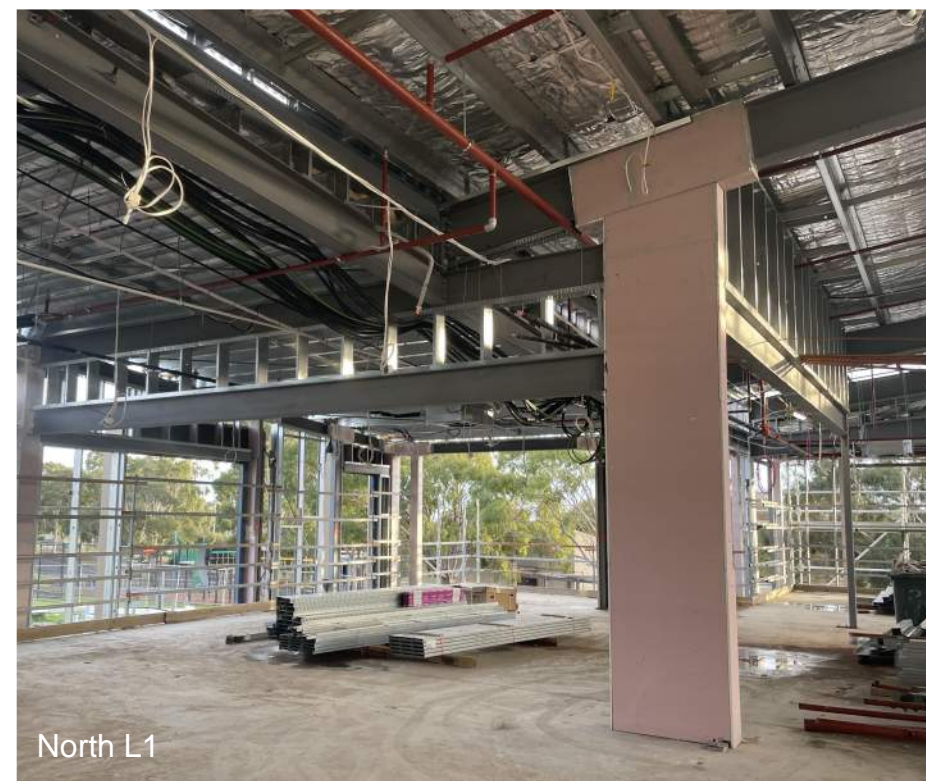

North L1



South L2



North West

After a busy fortnight with peak winter conditions, our team continues to progress through the chilled days. Along the West facade, all shrouds have now been installed. These vary in size, from over 3 metres tall to 1.8 metres. This allows brickwork to progress around to the West. Sarking has also been installed at ground level along the East pre-cast wall. Brickwork will then follow along the East, with scaffold almost complete to reach greater heights. Earlier in the week we also had two small concrete pours to the lids of both fire stairs 1 & 2.

In the lecture theatre, the tiered seating work continues. Condeck reinforcement has been installed on top of the existing blockwork. On level 1 North, fireproofing to columns has been underway. On all levels, service rough-in continues, including electrical, security and dry fire. Plaster sheeting has also commenced to the North building which proves the advancement of the project.



West



North L1



East



Lecture Theatre- GF

COMPLETED TASKS

- Commence sarking wrap to East pre-cast wall.
- Structural steel all but complete
- Fire stair lids 1&2 poured
- Installation of mechanical units for toilets
- North scaffold for continuation of brickwork
- Window shroud install

UPCOMING TASKS

- Complete wall framing on North level 1
- Complete roofing to south level 2
- Complete brickwork
- Complete all internal stair pours
- Commence link ways to existing structure

YOUR PROJECT TEAM



Alex Simpson
Project Manager



Paul Hunt
Site Manager



Adam McPhee
Site Manager



Jacob Bunn
Senior Contract Administrator



Caroline Andrus
Contract Administrator



Brett Benson
Site Coordinator
